



**DELIBERASAUN N. 109/VIII/CAFI/2025**

Conselho de Administração do Fundo das Infraestruturas – CAFI, bazeia ba artigo 10º (1) e (3) DL Nº. 25/2024, de 22 de maio, Primeira Alteração ao DL Nº.13/2016, 18 de Maio, realiza reuniaun Ordinária iha loron Sexta-feira, 1 de Agosto de 2025, e halo deliberaun ba assunto tuir mai ne’e:

**Asuntu:** Pedido aprovasaun *Extensaun tempu, ba projetu Konstrusaun Moru Hadulas Altar Santo Tasi Tolu.*

**Proponente:** Ministério Planeamento e Investimento Estratégico – MPIE

**Notas/justifikasaun:**

- Asuntu refere apresenta iha reuniaun CAFI iha dia 1 de Agostu de 2025, ne’ebi apresenta husi ADN,I.P. ba projetu refere;
- Bazeia ba karta husi ADN, I.P. ho no ref.: 392/ADN/UCVQ/VII/2025, data 23 de julho de 2025, ho asuntu Pedidu Extensaun Tempu Kontratu, Robena Unip. Lda;
- Bazeia ba karta pedidu husi kompanhia Robena Unipessoal, Lda, ho no. ref.: 008/Rb/VII/2025, data 8 de julho de 2025, ho asuntu, Pedidu Extensaun Kontratu I ba Projetu Konstrusaun Moru Hadulas Altar Santo Tasi Tolu;
- Bazeia ba pedidu extensaun kontratu ne’ebi hato’o husi kompanhia Robena Unip. Lda ba projetu Konstrusaun Moru Hadulas Altar Santo Tasi Tolu, ne’ebi nia ezekuta servisu hahu 19 de dezembru de 2024, labele finaliza tuir tempu kontratu original dia 19 de julho de 2025 (fulan 8) atinzi 40%, ho razaun iha espesifikasiada balun ne’ebi latuir kontratu, no deside suspende servisu durante fulan 2 (marsu 2025-maio 2025);
- Ho razaun ne’ebi temi iha paragrafu anterior, ADN, I.P. husu atu fo konsiderasaun hodi extende kontratu (Amendment – 1) ba kompanhia Robena Unip. Lda to’o 31 de dezembro de 2025 hodi finaliza servisu to’o 100%;
- Alokasaun orsamentu iha FI 2025: \$0, Programa 980: Inclusão Social, kodigu atividade 9805313:Konstrusaun Foun Moru Hadulas Altar Santo Tasi-Tolu, kontratu original: \$937,087.55, balansu: \$830,442.15, halo ona Pagamentu iha tinan 2024, \$106,645.40, ekivale 11.38%;
- Projetu nain sei assume responsabilidade hodi assegura orsamentu ba Ezekusaun no Implementasaun projetu;



**IX GOVERNO CONSTITUCIONAL**  
**MINISTÉRIO DO PLANEAMENTO E INVESTIMENTO ESTRATÉGICO**  
**FUNDO DAS INFRAESTRUTURAS**



Conselho de  
Administração

- Projetu nain konfirma katak sei asume responsabilidade ba monitorizasaun e akompanhamentu ba ezekusaun projetu ne'e no sei garante kualidade servisu nian tuir padraun no espesifikasiakaun ne'ebi aprova ona;

- Lista proposta:

Naran projeto/valor kontratu original	Extensaun tempu	Alokasaun orsamentu iha FI 2025
<ul style="list-style-type: none"> <li>• Konstrusaun Moru Hadulas Altar Santo Tasi Tolu;</li> <li>• <i>Kontratu original</i> \$937,087.55.</li> </ul>	<ul style="list-style-type: none"> <li>• EoT: 31 de dezembru 2025</li> </ul>	<ul style="list-style-type: none"> <li>• Programa 980: Inclusão Social,</li> <li>• Kodigu atividade 9805313: Konstrusaun Foun Moru Hadulas Altar Santo Tasi-Tolu,</li> <li>• Alokasaun orsamentu iha FI 2025: \$0,</li> <li>• Kontratu original: \$937,087.55, balansu: \$830,442.15, halo ona Pagamentu iha tinan 2024, \$106,645.40, ekivale 11.38%;</li> </ul>

**Rekomendasaun:**

CAFI atu aprova Extensaun tempu bazeia ba justifikasaun sira ne'ebi hato'o ona iha leten ba projetu ***Konstrusaun Moru Hadulas Altar Santo Tasi Tolu***, bazeia ba pedidu husi MPIE/ADN, I.P. ho empreza ***Robena Unip. Lda***,

**Desizaun:**

1. CAFI aprova Extensaun tempu bazeia ba justifikasaun sira ne'ebi hato'o ona iha leten ba projetu ***Konstrusaun Moru Hadulas Altar Santo Tasi Tolu***, bazeia ba pedidu husi MPIE/ADN, I.P.;
2. Lista aprovasaun:

Naran Projeto/Empresa	Extensaun tempu	Orgaun Kompetênti Autoriza despezas - DL No. 23/2022, 19 de Maio
<ul style="list-style-type: none"> <li>• Konstrusaun Moru Hadulas Altar Santo Tasi Tolu;</li> <li>• Robena Unip. Lda</li> </ul>	<ul style="list-style-type: none"> <li>• EoT: 31 de marsu 2026</li> </ul>	CAFI: alinea 1 (b) Artigo 5.º Competência para a autorização da despesa.

*[Handwritten signatures]*



IX GOVERNO CONSTITUCIONAL  
MINISTÉRIO DO PLANEAMENTO E INVESTIMENTO ESTRATÉGICO  
FUNDO DAS INFRAESTRUTURAS



Conselho de  
Administração

Aprovado husi CAFI iha loron 1 de Agosto de 2025.

O Conselho de Administração do Fundo das Infraestruturas

O presidente,



Gastão Francisco de Sousa

Ministro do Planeamento e Investimento Estratégico

Santina José Rodrigues Ferreira Viegas Cardoso

Ministra das Finanças

(La Participa iha Reuniaun)



Miguel Marques Gonçalves Manetelu

Ministro dos Transportes e Comunicações



Samuel Marçal

Ministro das Obras Públicas

DELIBERASAUN N.º109/VIII/CAFI/2025



**IX GOVERNO CONSTITUCIONAL**  
**MINISTÉRIO DO PLANEAMENTO E INVESTIMENTO ESTRATÉGICO**  
**FUNDO DAS INFRAESTRUTURAS**



**Conselho de  
Administração**

**Annexo:**

Dili, de Julho de 2025

No Ref : 565/ADN/UCVQ/VII/2025

Hato' o ba : Exmo. Sr. Eng. Januario Maia Guterres  
Diretor Adjunto no Diretor Executivo Interino - ADN, I.P.


Assunto : Pedidu Extensaun Tempo Kontratu, Robena Unip. Lda

Ho Respeito,

Relasiona ho Assunto refere iha leten Hakarak imforma ba Diretor Adjunto no Diretor Executivo Interino - ADN,I.P. Katak Bazeia ba pedidu extensaun kontatu nebe'e hato'o husi Kompanhia **Robena Unip. Lda Ba Projeto Konstrusaun Moru Hadulas Altar Santo Tasitolu**, Nebée Ezekuta servisu sira nebe hahu iha dia 19 de Dezembru de 2024, Labele finaliza tuir tempu kontratu original ha dia 19 de jullu 2025 (durante fulan ualu nia laran), Atinji progresu 40.00%. Ho razaun tambo durante iha implementasaun infrenta problema ba servisu Betaun, nebe kualidade la to'o 21 Mpa no instalasaun besi nebe la tuir spesifikasi, Quaze fulan rua liu servisu suspende hodi hein desizaun. Molok kontinua fali servisu (**tempu suspende Marsu – Maio 2025**).

Depois halo verifikasi saun no diskusaun ba mudansa husi planu servisu nebe kompanhia hato'o (S Curve), katak kompanhia presija tempu hodi finaliza servisu iha terrenu hanesa : Parte Civil (Instala Cyclope, Beam, lintel beam, wall block, Plester no Painting), Eletrikal nomos material BRC nebe tenki sosa husi nasau Indonesia. Nune'e tambo kestaun tempu no garante atu servisu refere bele finaliza ho kualidade nebe diak tuir Spesifikasi saun nebe iha dokumentus Kontratu. Relata ba Diretor Adjunto no Diretor Executivo Interino ADN,I.P Hodi bele fo konsiderasaun ba fasilita extensaun kontratu (Amandament –1) ba Kompanhia Robena Unip. Lda to'o 31 Dezembro Hodi Finaliza servisu to'o 100%

Mak ne'e deit ba ita bo'ot nia atensaun hato'o agradesimentu wa'ain no subskreve ho konsiderasaun a'as tebes.



Arch. Francisco Xavier de Deus Jeronimo  
Coordenador UCVQ - ADN, I.P.

*schaduwle  
Prog am  
Fur  
bale  
tba  
agente  
nu  
CATI  
23/7/25*



Díli, 21 Julu 2025

Nú. Ref. : 310 EPAS - ADN,I.P/ /VII/2025

Hato'o ba : Arch. Francisco X. De Deus Jeronimo  
Coordenador UCVQ - ADN, I.P

Assunto : Extensaun tempo Kontratu, Robena Unip. Lda

Ho respeito,

Liu husi óficio ne'e relata ba Chefi Departemento EPAS ADN.IP katak baseia ba pedidu Extensaun Kontrato I nebe'e hato'o husi kompamhia **Robena Unip.Lda.** ba projeto **Konstrusaun Moru Hadulas Altar Santo Tasitolu** ida nebe ejekuta servisu nebe hahu iha **19 Desembru 2024**, labele finaliza tuir tempo kontratu original iha **19 Julu 2025** (durante fulan ualu), atinji progresu **40.00%**. ho razaun tamba durante iha implementasaun infrenta problema ba servisu Betaun, nebe kualidade la to'o 21Mpa no instalasaun besi nebe la tuir Spesifikasiasaun, Quaze fulan rua liu servisu suspende hodi hein desijaun. Molok kontinua fali servisu (**tempu suspende Marsu – Maio 2025**).

Depois halo verifikasiasaun no diskusaun ba mudancas husi planu servisu nebe kompañia hato'o (S Curve), katak kompañia presija tempu hodi finaliza servisu iha terrenu hanesan: parte Civil (instala Cyclope, beam, lintel beam, wall block, Plester no Painting), Elektrikal nomos material BRC nebe tenki sosa husi Nasaun Indonesia. Nune'e tamba kestaun tempu no atu garante hodi servisu refere bele finaliza ho kualidade nebe diak tuir spesifikasiasaun nebe iha dokumentos kontratu.

Relata ba Sr. Cordenador hodi hato'o ba Director Adjunto no Director Executivo interino ADN, IP hodi bele fó konsiderasaun ba fasilita extensaun kontratu (amandament-1) ba kompañia Robena Unip. Lda to'o **31 dezembru 2025** hodi finaliza servisu to'o 100%.

Mak ne'e de'it, ba atensaun no kolaborasaun diak la haluha hato'o obrigado wa'in

  
Egidio Gonçalves  
Chefe Departemento EPAS ADN, I.P

Dili, 21 Julu 2025

Hato'o ba : Eng. Egidio Gonçalves  
Chefe Departamento EPAS ADN,I.P

Husi : Eng. Agustinho Aranda   
Eng. Rosalia de Fatima   
Arch. Zulkarnaen Depari   
Eng. EPAS ADN, I.P Municipio Dili

Assuntu : Pedidu Aprovasaun Extensaun Tempu Kontratu

Ho Respeitu,

Liu husi óficio ne'e relata ba Chefi Departamento EPAS ADN.IP katak baseia ba pedidu Extensaun Kontrato I nebe'e hato'o husi kompamhia **Robena Unip.Lda.** ba projeto **Konstrusaun Moru Hadulas Altar Santo Tasitolu** ida nebe ejekuta servisu nebe hahu iha **19 Desembru 2024**, labele finaliza tuir tempo kontratu original iha **19 Julu 2025** (durante fulan ualu), atinji progresu **40.00%**. ho razaun tamba durante iha implementasaun infrenta problema ba servisu Betaun, nebe kualidade la to'o 21Mpa no instalasaun besi nebe la tuir Spesifikasi, Quaze fulan rua liu servisu suspende hodi hein desijaun. Molok kontinua fali servisu (**tempu suspende Marsu – Maio 2025**).

Depois halo verifikasi no diskusaun ba mudancas husi planu servisu nebe kompañia hato'o (S Curve), katak kompañia presija tempu hodi finaliza servisu iha terrenu hanesan: parte Civil (instala Cyclope, beam, lintel beam, wall block, Plester no Painting), Elektrikal nomos material BRC nebe tenki sosa husi Nasaun Indonesia. Nune'e tamba kestaun tempu no atu garante hodi servisu refere bele finaliza ho kualidade nebe diak tuir spesifikasi nebe iha dokumentos kontratu, ekipa tekniku EPAS, deside hodi husu ba superior ADN,IP atu fasilita extensaun kontratu (amandament-1) ba kompañia Robena Unip. Lda to'o **31 dezembru 2025** hodi finaliza servisu to'o 100%.

Mak ne'e de'it, ba atensaun no kolaborasaun diak la haluha hato'o obrigado wa'in

\*aneksu pedidu extensaun kompañia



## **FORMULARIO DE DESPACHO**

Unidade de Controlo e Validação de Qualidade (UCVQ)

Naran Projeto

: Konstruksi Monumen Hukum Aceadorus Altar Tari tol  
Municipio Dili

Kompanhia /Departamento : Robena Unip. Ida

## Projeto nain /Husi :KomPanhia

**Assunto** : Pedido External - controle 1.

## **DESPACHO Ba**

- Departamento Edificio Publico, Agua e Saneamento
  - Departamento Infrastruktura, Transportes e Irrigasaun
  - Departamento ITC, Mecanical e Elektrika
  - Departamento Laboratoriu
  - Administrasaun - UCVO

Orijinal	Kopia
	<input type="checkbox"/>
	<input type="checkbox"/>
	<input type="checkbox"/>
	<input type="checkbox"/>
	<input type="checkbox"/>

➤ Despacho/Instrusaun : URGENTE, IMPORTANTE, NORMAL

Versilia e Justi filha no Relato mai  
cordeiro. (esta molto libera)

Bn ay. Municipio Dili (kontraktor), aflu:

Data Despacho. 02/07/2018

## Asinatura

- Verifikasi didik kota perstifikasi
- Responde no perstifika tempo extansu, thn teknis teknis
- Kordinasi ke drpt EPAS.

(Arch. Francisco Xavier de Deus Jeronimo)

Ko'ordenador . UCVQ



AGÊNCIA DE DESENVOLVIMENTO NACIONAL, I. P.

## FORMULARIO DESPACHO

Data de Entrada Documentos: 30 / Jun / 2025	Data do Documentos: 30 / Jun / 2025
---	-------------------------------------

Husi: ROBENA UNIP, LDA
------------------------

No Ref : 008/Rb/VI/2025
-------------------------

<p>Projetu :</p> <p><b>P240998-Konstrusaun Moru Haleu Areadores Altar Tasi Tolu Municipio Dili</b></p>	<p>Quantidade Documentos : 1</p> <p>Anexo :</p>
<p>Assuntos :</p> <p><b>Pedido Extensaun Kontrato I.</b></p>	
<p>No. Tf : 77141127</p>	
<p>Companhia : Robena Unip, Lda</p>	
<p><b>Despacho :</b></p> <ul style="list-style-type: none"> <li><input type="radio"/> Unidade de Gestão Administrativa</li> <li><input type="radio"/> Unidade de Avaliação de Projectos</li> <li><input checked="" type="radio"/> Unidade de Controlo e Validação de Qualidade</li> <li><input type="radio"/> Unidade de Estudo e Desenvolvimento de Competências</li> <li><input type="radio"/> Adjunto</li> <li><input type="radio"/> Assessor/a</li> <li><input type="radio"/> Gabinete DE / Base de Dadus</li> <li><input type="radio"/> Other</li> </ul>	
<p><i>Yeru fito justificativa fo Relatorio.</i></p>	
<p>Data: ..... 1/7/25</p>	
<p style="text-align: right;"> Januario Maia Guterres Director Adjunto e Diretor Executivo Interino ADN,I.P.</p>	

Dili, 08 Julho 2025

No. Ref : 008 / Rb/VII/ 2025

Hato'o Ba : Ex <sup>mo.</sup> Sr. Januario Maia Guterres  
Diretor Adjunto e Diretor Executivo Interino – ADN.IP

Projeto : Konstrusaun Moru Haleu Areadores Altar Tasi Tolu Munisipio Dili

Àsunto : Pedido Extensaun Kontrato I

Ho respeito,

Baseia ba asunto iha leten tuir mai husi kompanha Robena Unipessoal Lda hato'o ba Sr. Diretor katak baseia ba Tempu ou Time Schedule iha Kontrato ne'ebe asina iha dia **19 Desembro 2024 no remata iha dia 19 Julho 2025**, maibe presentagem servisu iha terenu foin atinji **40 %** tamba ne'e kompanha husu atu extende tan tempu ba kontrato hodi bele finaliza servisu iha terenu ba 100 %. Razaun halo extensaun tempu mak hanesan tuir mai ne'e:

1. Suspensaun servisu husi parte tekniku ADN-IP durante fulan Marco to'o iha Maio mak foin halo kontinuasaun servisu iha terenu tumba kestaun Mix Desain betaun.
2. Spesifikasiacaun ba Pembesian ringball iha terenu la tuir BoQ nune'e difikulta kompanha atu aselera servisu iha terenu no presija atu troka no tuir fali Spesifikasiacaun iha BoQ no fo impaktu ba tempu servisu.
3. Kondisaun iklima hanesan tempu udan ne'ebe mak fo impaktu ba progresso servisu iha terenu. *Anexo dadus Udan Be'en*
4. Material BRC ne'ebe mak parte kompanha presija order ou Haruka husi Nasaun Vijinhu Indonesia nune'e presija tempu atu halo instalasaun iha terenu. Tuir planu Material BRC sei to'o iha Timor iha Fulan Julho nia laran no hahu instalasaun iha fulan Agusto to'o Outubro.
5. Servisu *Finishing* nian ba *Plestering* no *Painting* tuir planu sei finaliza iha fulan Outubro to Novembro nia laran.




---

Ho razaun sira hanesan temi iha leten parte kompanha husu extensaun Kontrato I hahu husi data *20 Julho 2025 to dia 31 Desembro 2025 durante fulan 6 nia laran* baseia Time Schedule foun hanesan iha anexu. Parte kompanha husu extensaun kontrato to iha fulan Desembro 2025 tamba razaun prosesu administrativu dokumentus final entrega ba Dono do Projetu maibe fisikamente projetu refere bele finaliza iha fulan Novembro 2025 nia laran.

Mak ne'e deit ba atensaun no konsiderasaun la haluha hato'o obrigado Obrigado wain.

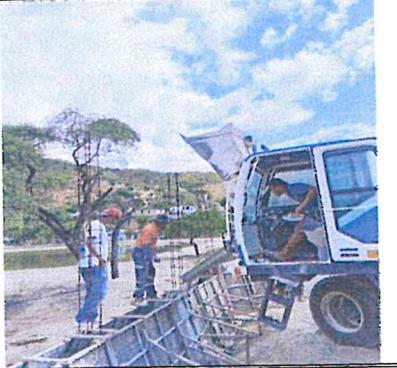
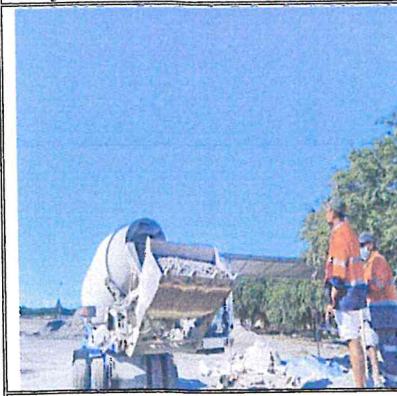
Ho Respeitu,

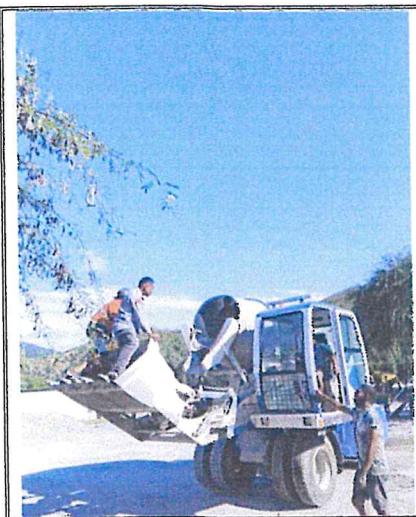


# PROGRESS PHOTOGRAPHS

## Construction Works On June 2025

### 1. Prosesu Servisu

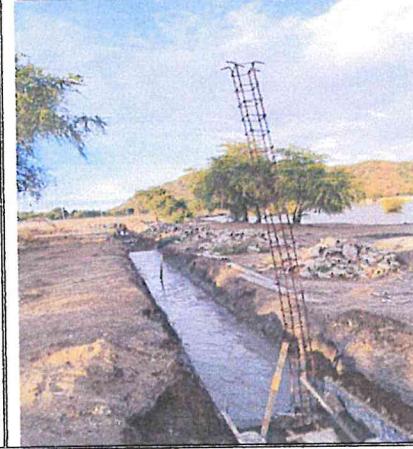
		
Location: Date: 02-06-2025 Subject: Cyclope Grupo 3	Location: Date: 02-05-2025 Subject: Cyclope Grupo 3	Location: Date: 02-05-2025 Subject: Cyclope Grupo 3
		
Location: Grupo 5 Date: 04-06-2025 Subject:	Location: Date: 04-06-2025 Subject: Material ADN	Location: Date: 04-06-2025 Subject: Trial Sampel Column & Sloof
		
Location: Date: 04-06-2025 Subject: Trial Sampel Column & Sloof	Location: Date: 04-06-2025 Subject: Trial Sampel Column & Sloof	Location: Date: 04-06-2025 Subject: Trial Sampel Column & Sloof



Location:  
Date: 04-06-2025  
Subject: Trial Sampel Column & Sloof

Location:  
Date: 04-06-2025  
Subject: Trial Sampel Column & Sloof

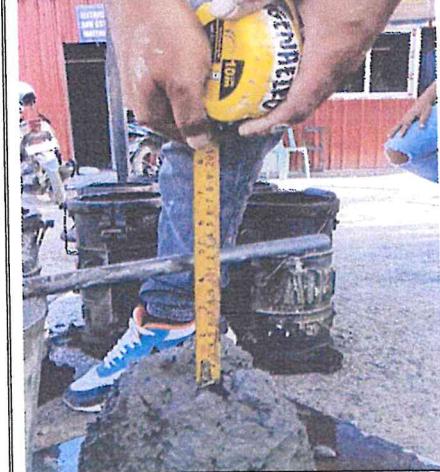
Location:  
Date: 04-06-2025  
Subject: Trial Sampel Column & Sloof



Location:  
Date: 04-06-2025  
Subject: Trial Sampel Column & Sloof

Location: Grupo 6  
Date: 04-06-2025  
Subject: Cor Lean Concrete

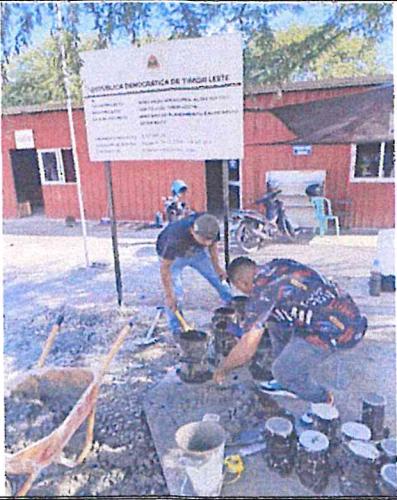
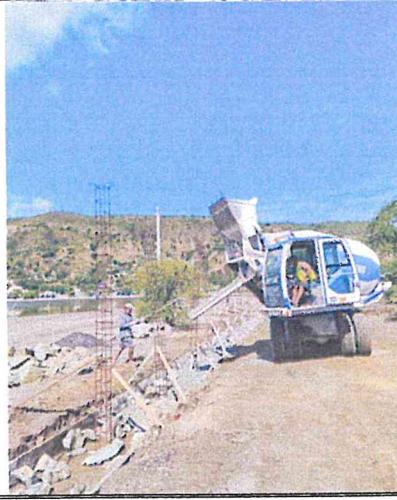
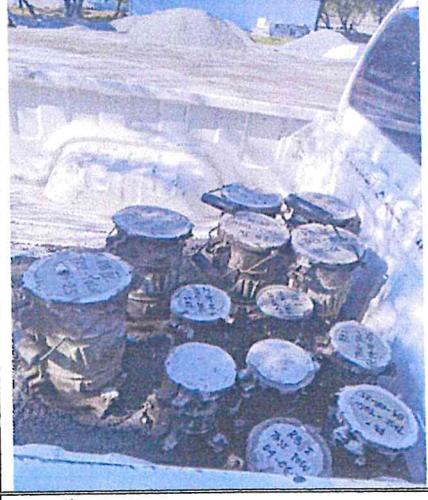
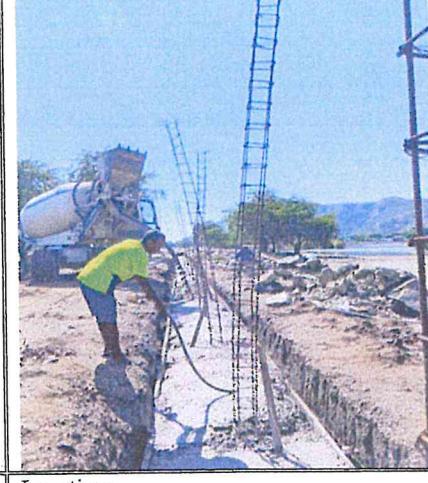
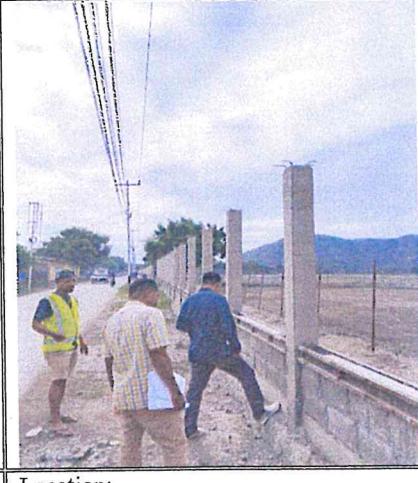
Location: Grupo 5  
Date: 04-06-2025  
Subject:

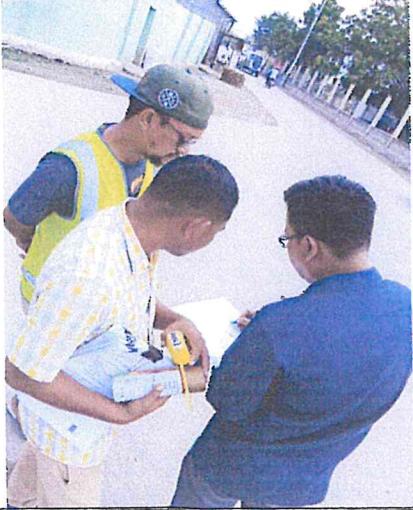
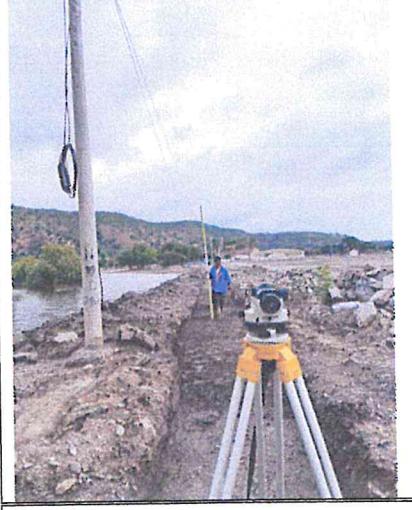
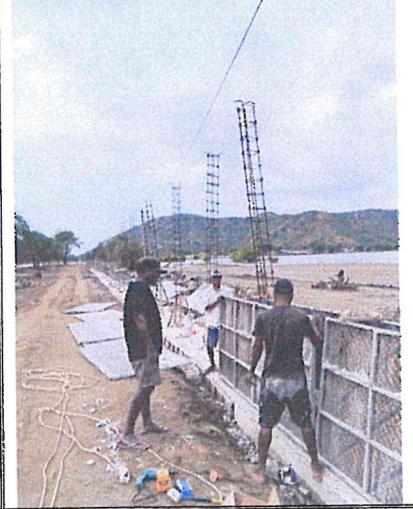
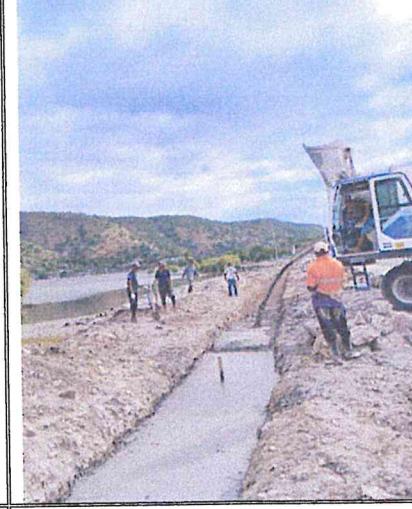
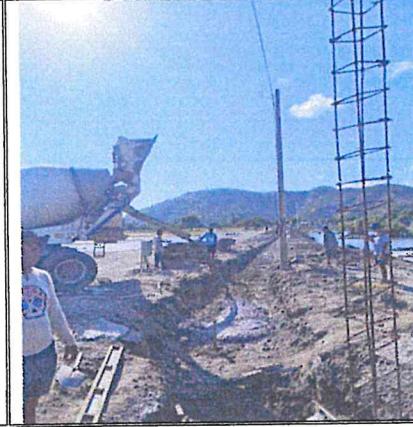
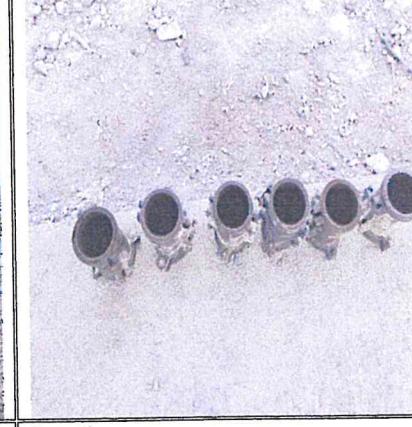


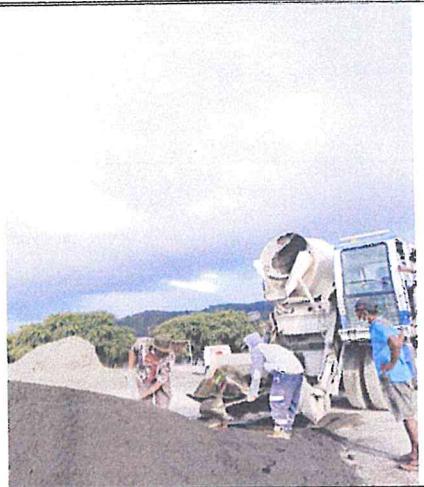
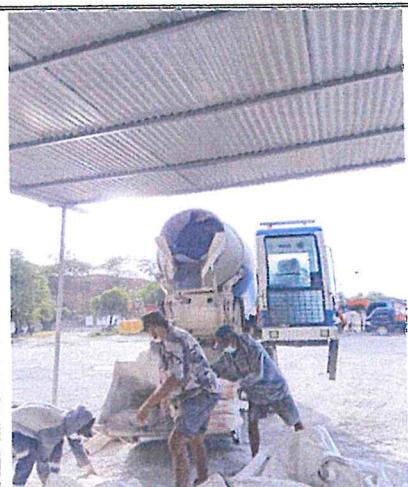
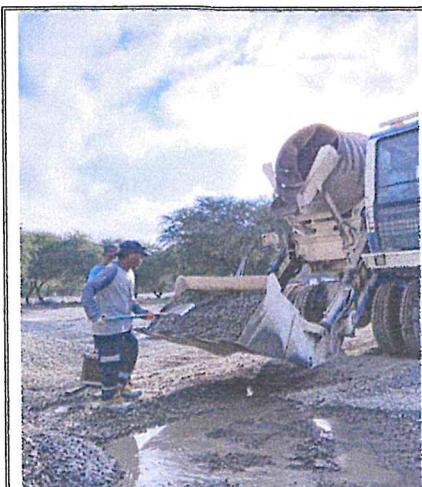
Location:  
Date: 05-06-2025  
Subject: Material ADN

Location:  
Date: 05-06-2025  
Subject: Trial Sampel 4 Cyclope

Location:  
Date: 05-06-2025  
Subject: Trial Sampel 4 Cyclope

		
<p>Location: Date: 05-06-2025 Subject: Trial Sampel 4 Cyclope</p>	<p>Location: Grupo 5 Date: 05-06-2025 Subject:</p>	<p>Location: Date: 06-06-2025 Subject: Sampel Cyclope, Column &amp; Sloof</p>
		
<p>Location: Date: 06-06-2025 Subject:</p>	<p>Location: Date: 07-06-2025 Subject:</p>	<p>Location: Date: 07-06-2025 Subject:</p>
		
<p>Location: Date: 08-06-2025 Subject:</p>	<p>Location: Date: 08-06-2025 Subject:</p>	<p>Location: Date: 10-06-2025 Subject:</p>

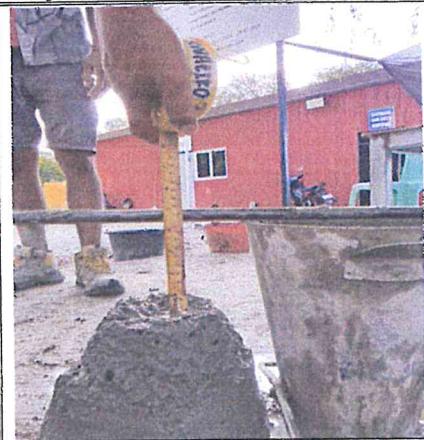
		
<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 10-06-2025 Subject:</p>
		
<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 11-06-2025 Subject:</p>
		
<p>Location: Date: 12-06-2025 Subject:</p>	<p>Location: Date: 13-06-2025 Subject:</p>	<p>Location: Date: 13-06-2025 Subject:</p>



Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

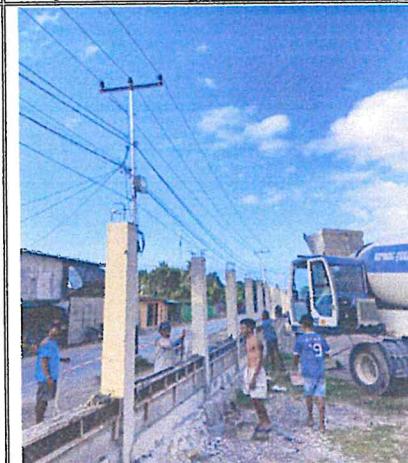
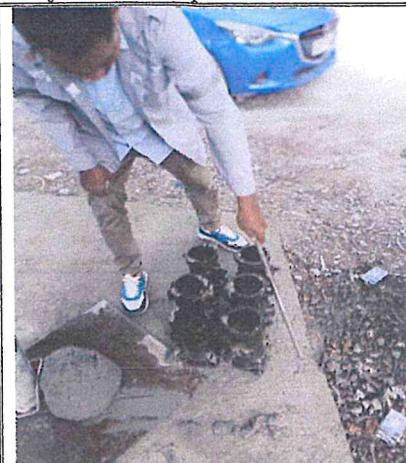
Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof



Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

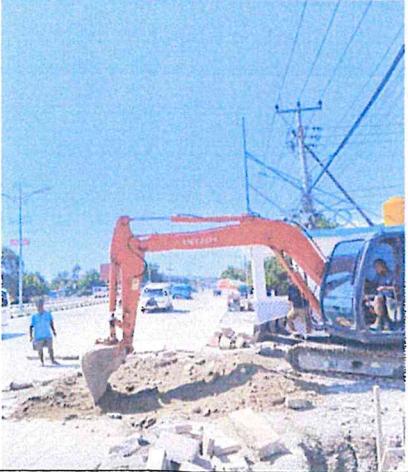
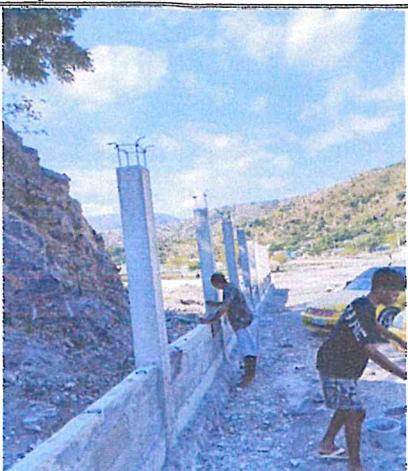
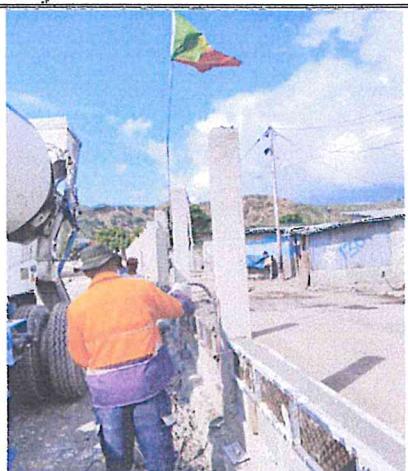
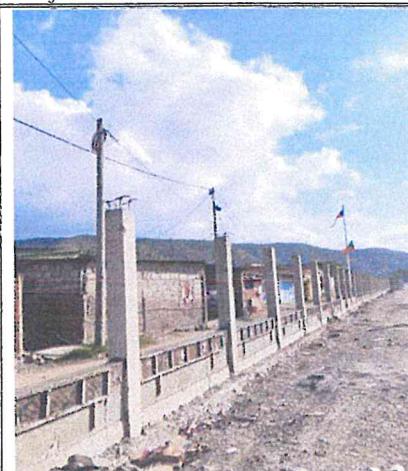
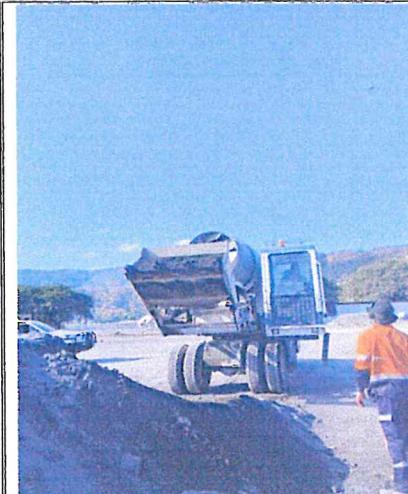
Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

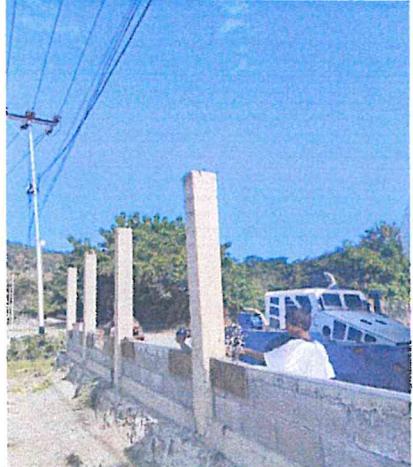
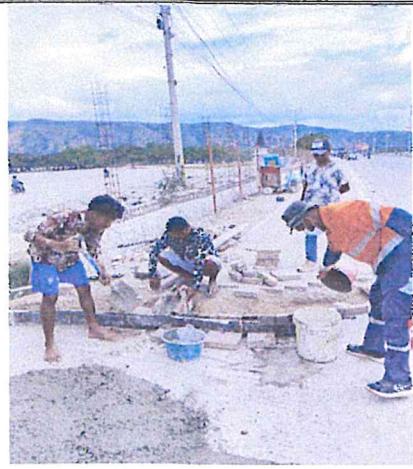
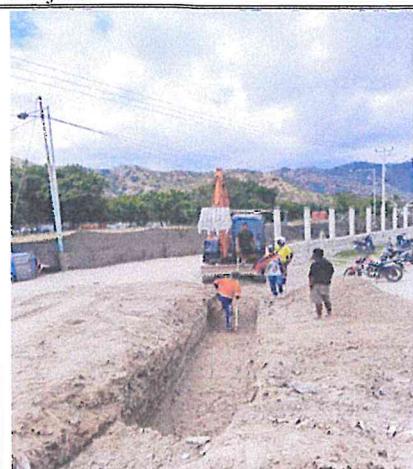
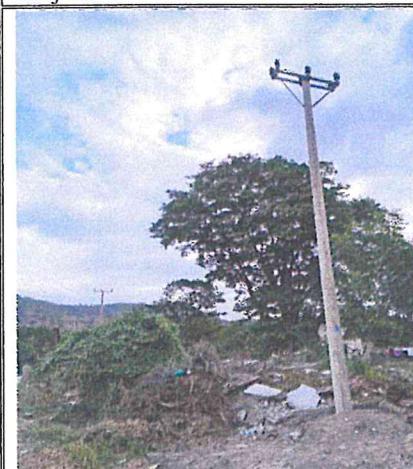


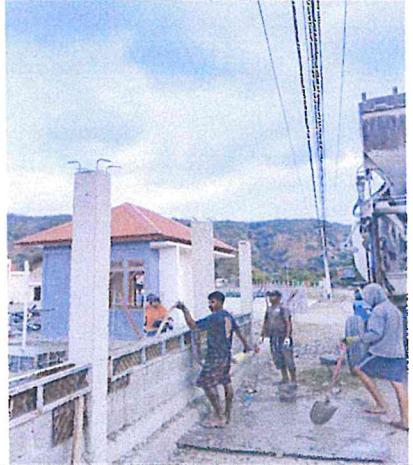
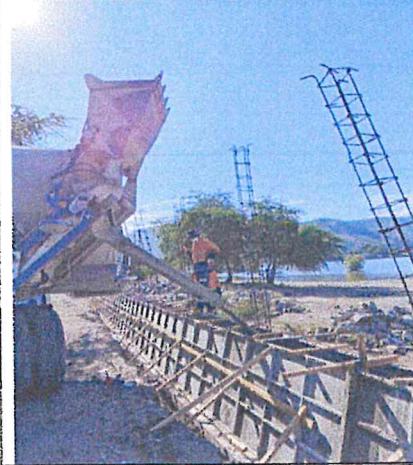
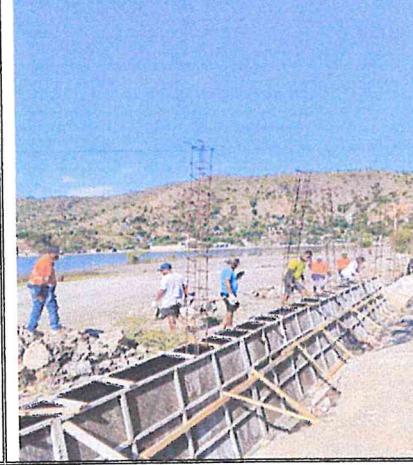
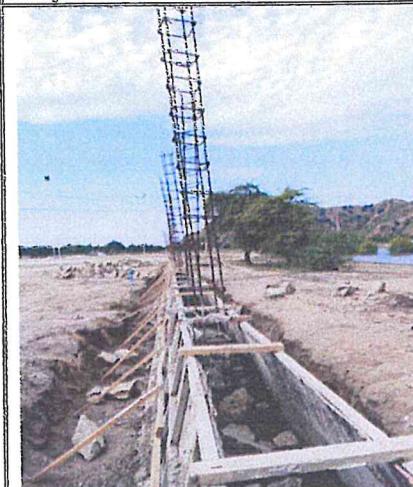
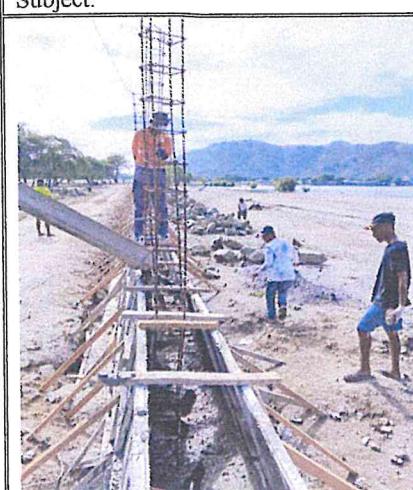
Location:  
Date: 13-06-2025  
Subject:Trial Sampel Column & Sloof

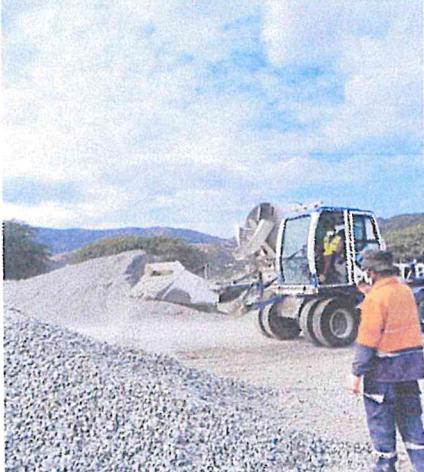
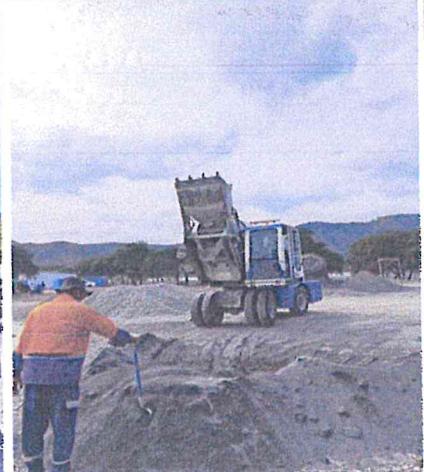
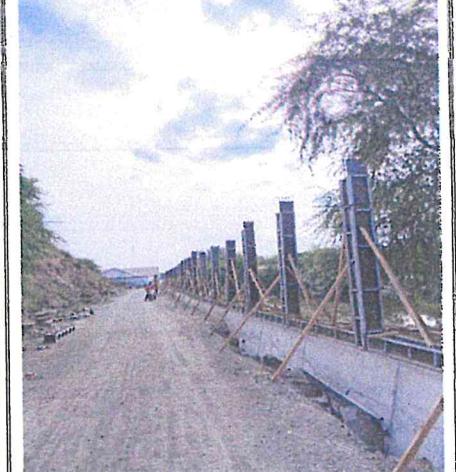
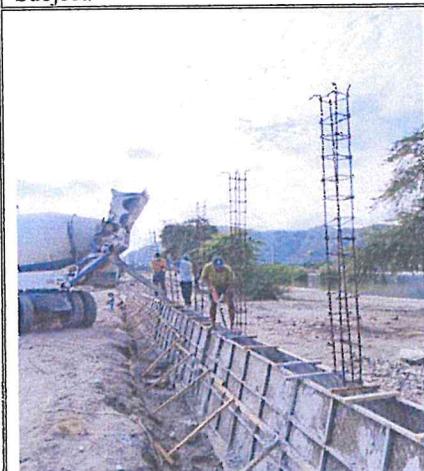
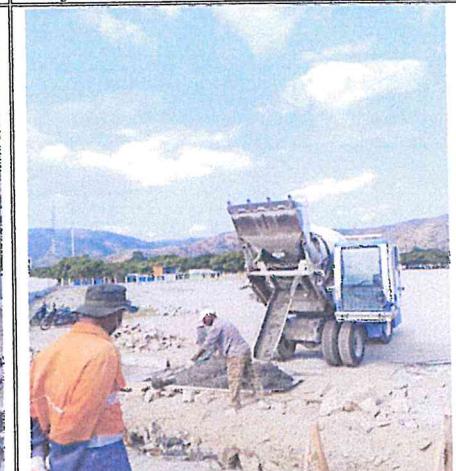
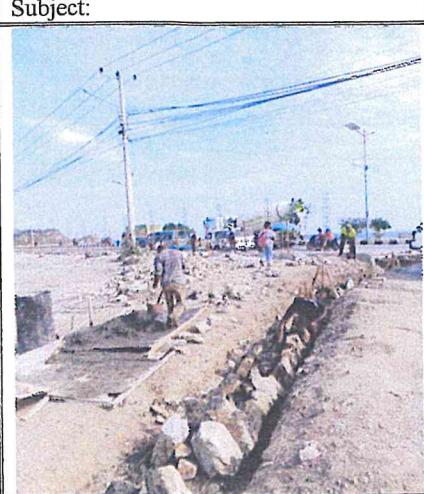
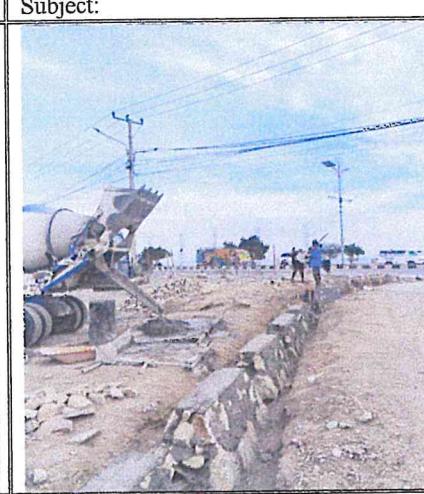
Location:Pameran  
Date: 13-06-2025  
Subject:

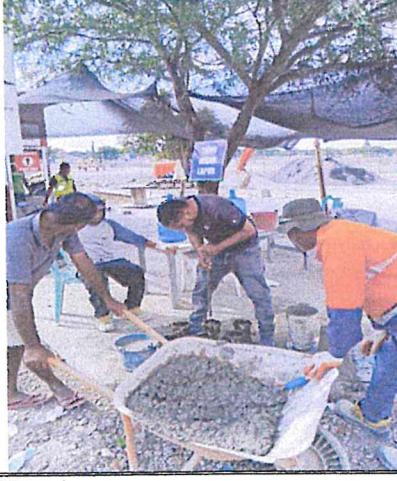
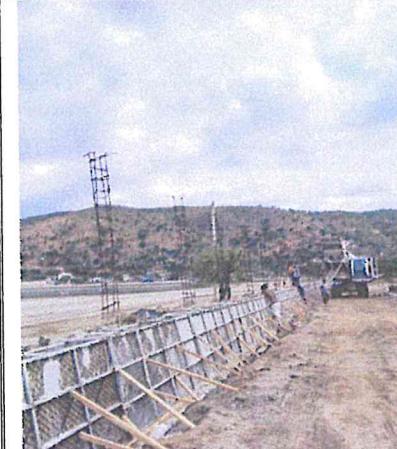
Location:Pameran  
Date: 13-06-2025  
Subject:

		
<p>Location: Date: 14-06-2025 Subject:</p>	<p>Location: Date: 14-06-2025 Subject:</p>	<p>Location: Date: 14-06-2025 Subject:</p>
		
<p>Location: Date: 18-06-2025 Subject:</p>	<p>Location: Date: 18-06-2025 Subject:</p>	<p>Location: Date: 18-06-2025 Subject:</p>
		
<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 19-06-2025 Subject:</p>

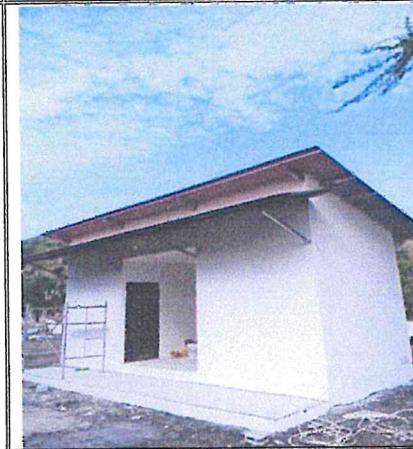
		
<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 19-06-2025 Subject:</p>
		
<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 19-06-2025 Subject:</p>	<p>Location: Date: 23-06-2025 Subject:</p>
		
<p>Location: Date: 23-06-2025 Subject:</p>	<p>Location: Date: 23-06-2025 Subject:</p>	<p>Location: Date: 23-06-2025 Subject:</p>

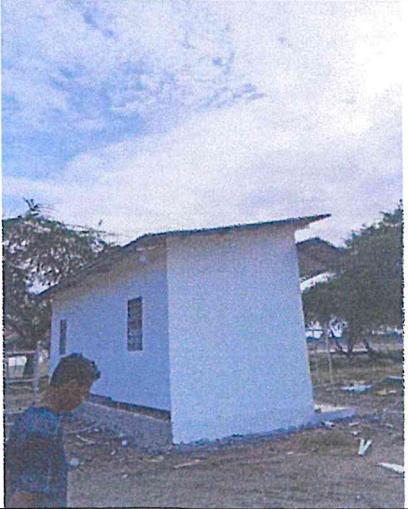
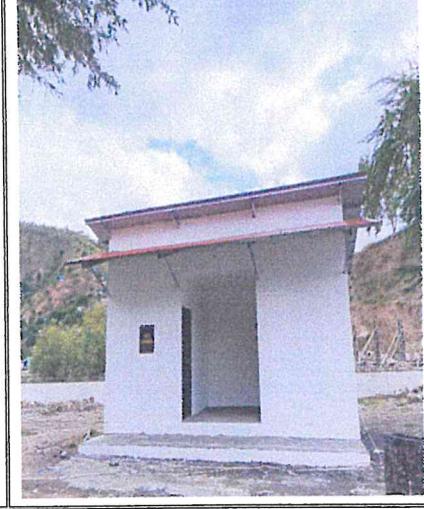
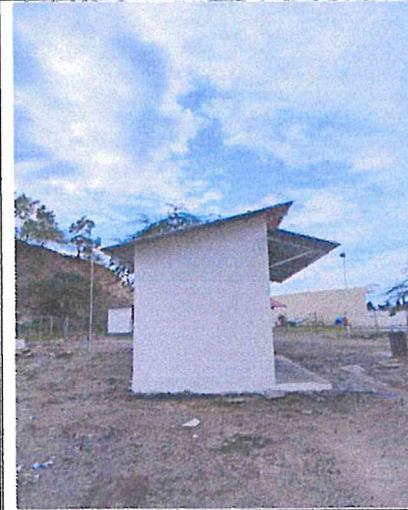
		
<p>Location: Date: 23-06-2025 Subject:</p>	<p>Location: Date: 24-06-2025 Subject:</p>	<p>Location: Date: 24-06-2025 Subject:</p>
		
<p>Location: Date: 24-06-2025 Subject:</p>	<p>Location: Date: 25-06-2025 Subject:</p>	<p>Location: Date: 25-06-2025 Subject:</p>
		
<p>Location: Date: 25-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>

		
<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>
		
<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>
		
<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 26-06-2025 Subject:</p>	<p>Location: Date: 27-06-2025 Subject:</p>

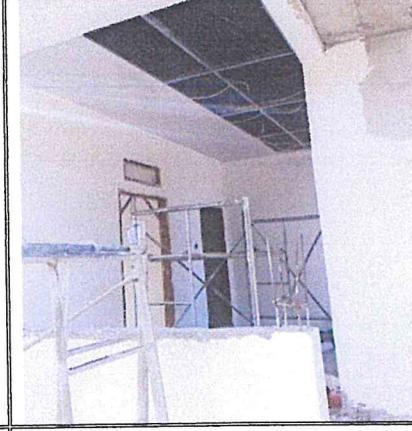
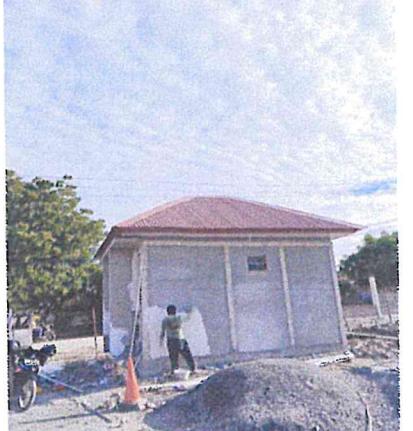
		
<p>Location: Date: 27-06-2025 Subject:</p>	<p>Location: Date: 27-06-2025 Subject:</p>	<p>Location: Date: 27-06-2025 Subject:</p>
		
<p>Location: Date: 27-06-2025 Subject:</p>	<p>Location: Date: 30-06-2025 Subject:</p>	<p>Location: Date: 30-06-2025 Subject:</p>
		
<p>Location: Date: 30-06-2025 Subject:</p>	<p>Location: Date: 30-06-2025 Subject:</p>	<p>Location: Date: 30-06-2025 Subject:</p>

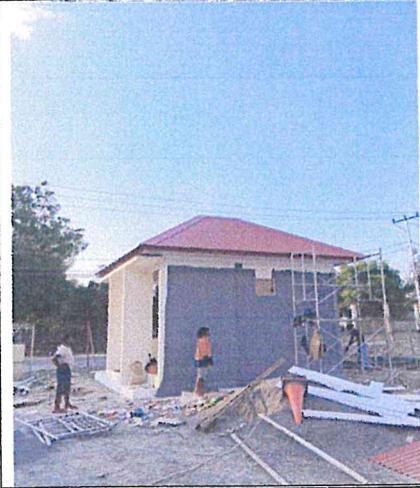
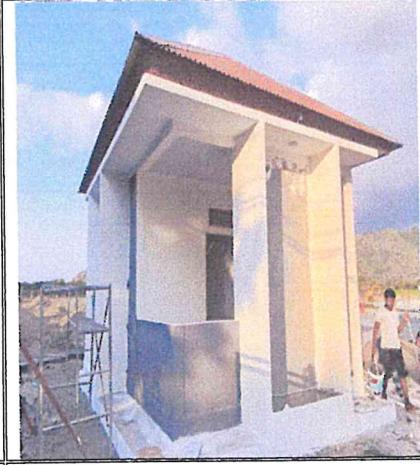
## 2. Prosessu Servisu Pos Seguransa THS-THM

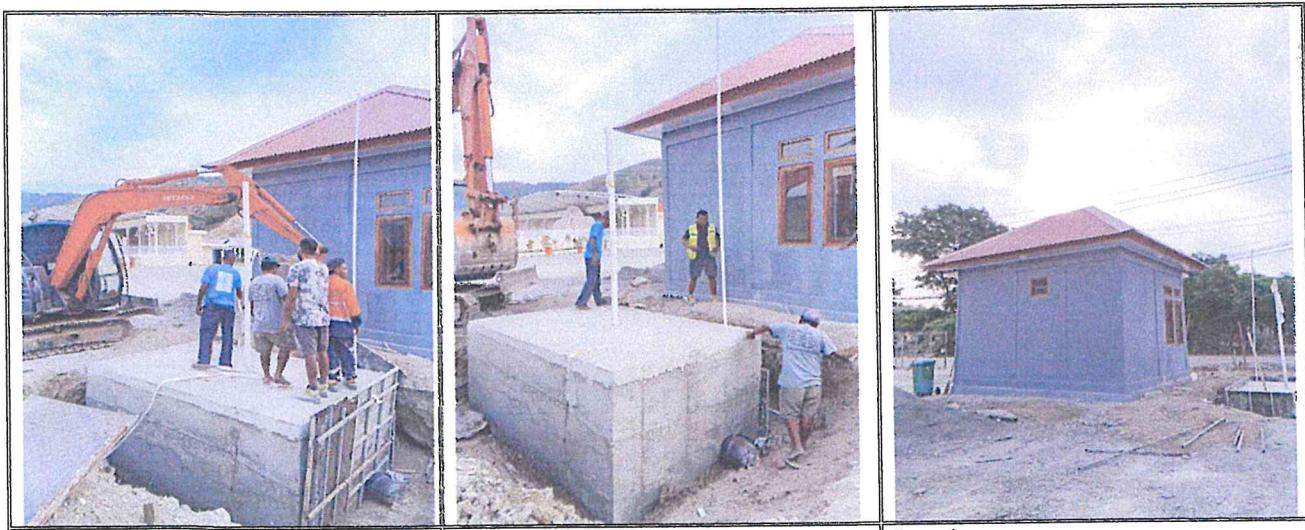
		
Location: Date: 02-06-2025 Subject:	Location: Date: 02-06-2025 Subject:	Location: Date: 02-06-2025 Subject:
		
Location: Date: 07-06-2025 Subject:	Location: Date: 07-06-2025 Subject:	Location: Date: 07-06-2025 Subject:
		
Location: Date: 07-06-2025 Subject:	Location: Date: 10-06-2025 Subject:	Location: Date: 10-06-2025 Subject:

		
<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 10-06-2025 Subject:</p>	<p>Location: Date: 12-06-2025 Subject:</p>
		
<p>Location: Date: 12-06-2025 Subject:</p>	<p>Location: Date: 12-06-2025 Subject:</p>	<p>Location: Date: 12-06-2025 Subject:</p>

### 3. Prosessu Servisu Pos Seguransa

		
Location: Date: 05-06-2025 Subject:	Location: Date: 05-06-2025 Subject:	Location: Date: 05-06-2025 Subject:
		
Location: Date: 05-06-2025 Subject:	Location: Date: 06-06-2025 Subject:	Location: Date: 06-06-2025 Subject:
		
Location: Date: 06-06-2025 Subject:	Location: Date: 06-06-2025 Subject:	Location: Date: 12-06-2025 Subject:

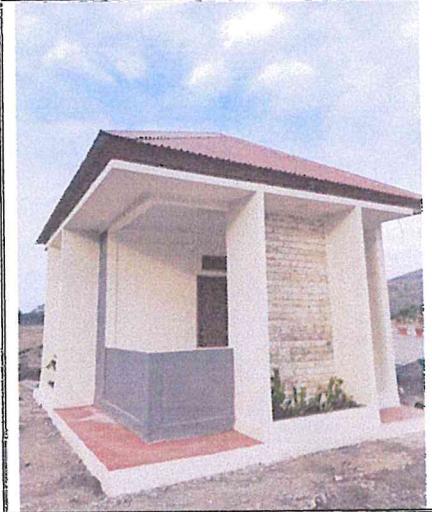
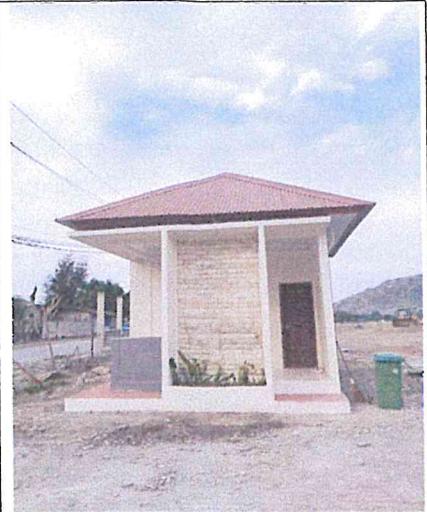
		
<p>Location: Date: 05-06-2025 Subject:</p>	<p>Location: Date: 17-06-2025 Subject:</p>	<p>Location: Date: 17-06-2025 Subject:</p>
		
<p>Location: Date: 17-06-2025 Subject:</p>	<p>Location: Date: 17-06-2025 Subject:</p>	<p>Location: Date: 23-06-2025 Subject:</p>
		
<p>Location: Date: 23-06-2025 Subject:</p>	<p>Location: Date: 23-06-2025 Subject:</p>	<p>Location: Date: 28-06-2025 Subject:</p>



Location:  
Date: 28-06-2025  
Subject:

Location:  
Date: 28-06-2025  
Subject:

Location:  
Date: 30-06-2025  
Subject:



Location:  
Date: 30-06-2025  
Subject:

Location:  
Date: 30-06-2025  
Subject:

## 2 - WEATHER REPORT



**Project:** Moru Haleu Areadores Altar Tasi Tolu

**Period :** From: : 1 June 2025      To : 30 June 2025

**Location :** Tasi Tolu

Time (Hours)	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	
Date	MORNING												AFTERNOON												
1	Sunday																								
2	Monday																								
3	Tuesday																								
4	Wednesday																								
5	Thursday																								
6	Friday																								
7	Saturday																								
8	Sunday																								
9	Monday																								
10	Tuesday																								
11	Wednesday																								
12	Thursday																								
13	Friday																								
14	Saturday																								
15	Sunday																								
16	Monday																								
17	Tuesday																								
18	Wednesday																								
19	Thursday																								
20	Friday																								
21	Saturday																								
22	Sunday																								
23	Monday																								
24	Tuesday																								
25	Wednesday																								
26	Thursday																								
27	Friday																								
28	Saturday																								
29	Sunday																								
30	Monday																								

LEGEND:

Fair (...hrs)

Cloudy (...hrs)

Light Rain (...hrs)  Heavy Rain (...hrs)



**Robena Unipessoal Lda**

High Quality Services

**Project:** Moru Haleu Areadores Altar Tasi Tolu

**Period :** From : 1 May 2025 To : 31 May 2025

**Location :** Tasi Tolu

Time (Hours)	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	
Date	Day	MORNING																							
1	Thursday																								
2	Friday																								
3	Saturday																								
4	Sunday																								
5	Monday																								
6	Tuesday																								
7	Wednesday																								
8	Thursday																								
9	Friday																								
10	Saturday																								
11	Sunday																								
12	Monday																								
13	Tuesday																								
14	Wednesday																								
15	Thursday																								
16	Friday																								
17	Saturday																								
18	Sunday																								
19	Monday																								
20	Tuesday																								
21	Wednesday																								
22	Thursday																								
23	Friday																								
24	Saturday																								
25	Sunday																								
26	Monday																								
27	Tuesday																								
28	Wednesday																								
29	Thursday																								
30	Friday																								
31	Saturday																								

**LEGEND:**

Fair (...hrs)

Cloudy (...hrs)

Light Rain (...hrs)

Heavy Rain (...hrs)



Project: Mori Halehu Areadore Altar Tasi Tok

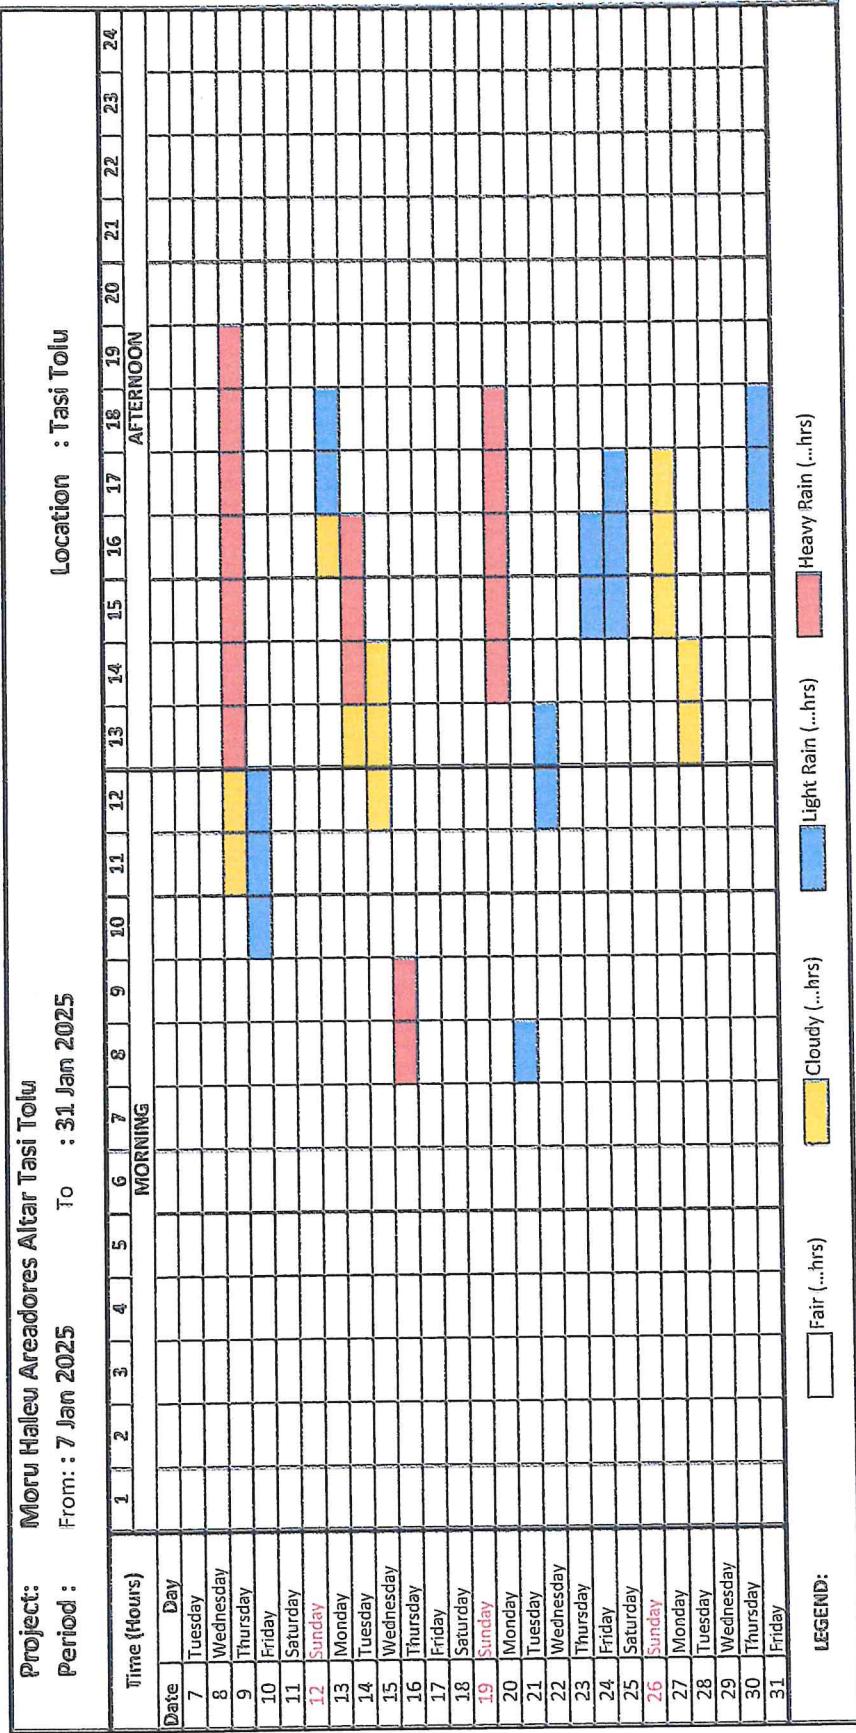
תְּנַשֵּׁא בְּנֵי כָּל־עֲמָדָה וְבְנֵי כָּל־עֲמָדָה

תְּנַשֵּׁא בְּנֵי כָּל־עֲמָדָה וְבְנֵי כָּל־עֲמָדָה



**Project:** Moru Haleu Areadores Altar Tasi Tolu  
**Period :** From : 7 Jan 2025 To : 31 Jan 2025

**Location :** Tasi Tolu



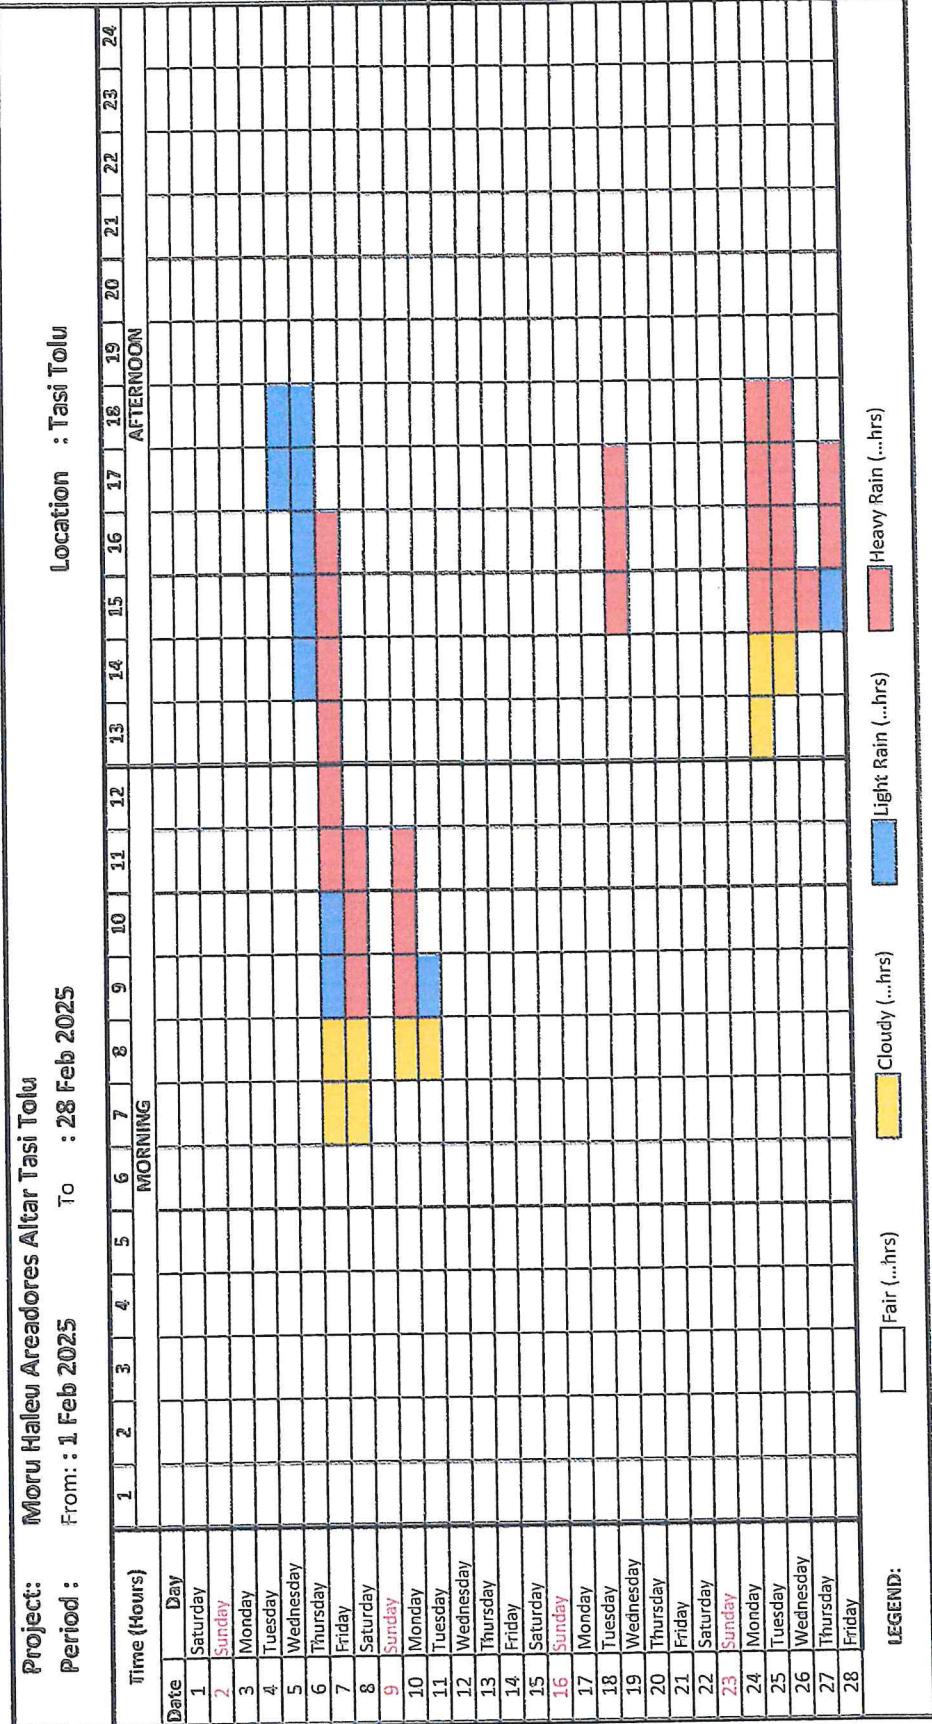
**Robena Engineering Team**  
 MOVING FORWARD WITH CONSTRUCTION



**Project:** Moru Haleu Areadores Altar Tasi Tolu

**Period :** From : 1 Feb 2025 To : 28 Feb 2025

**Location :** Tasi Tolu



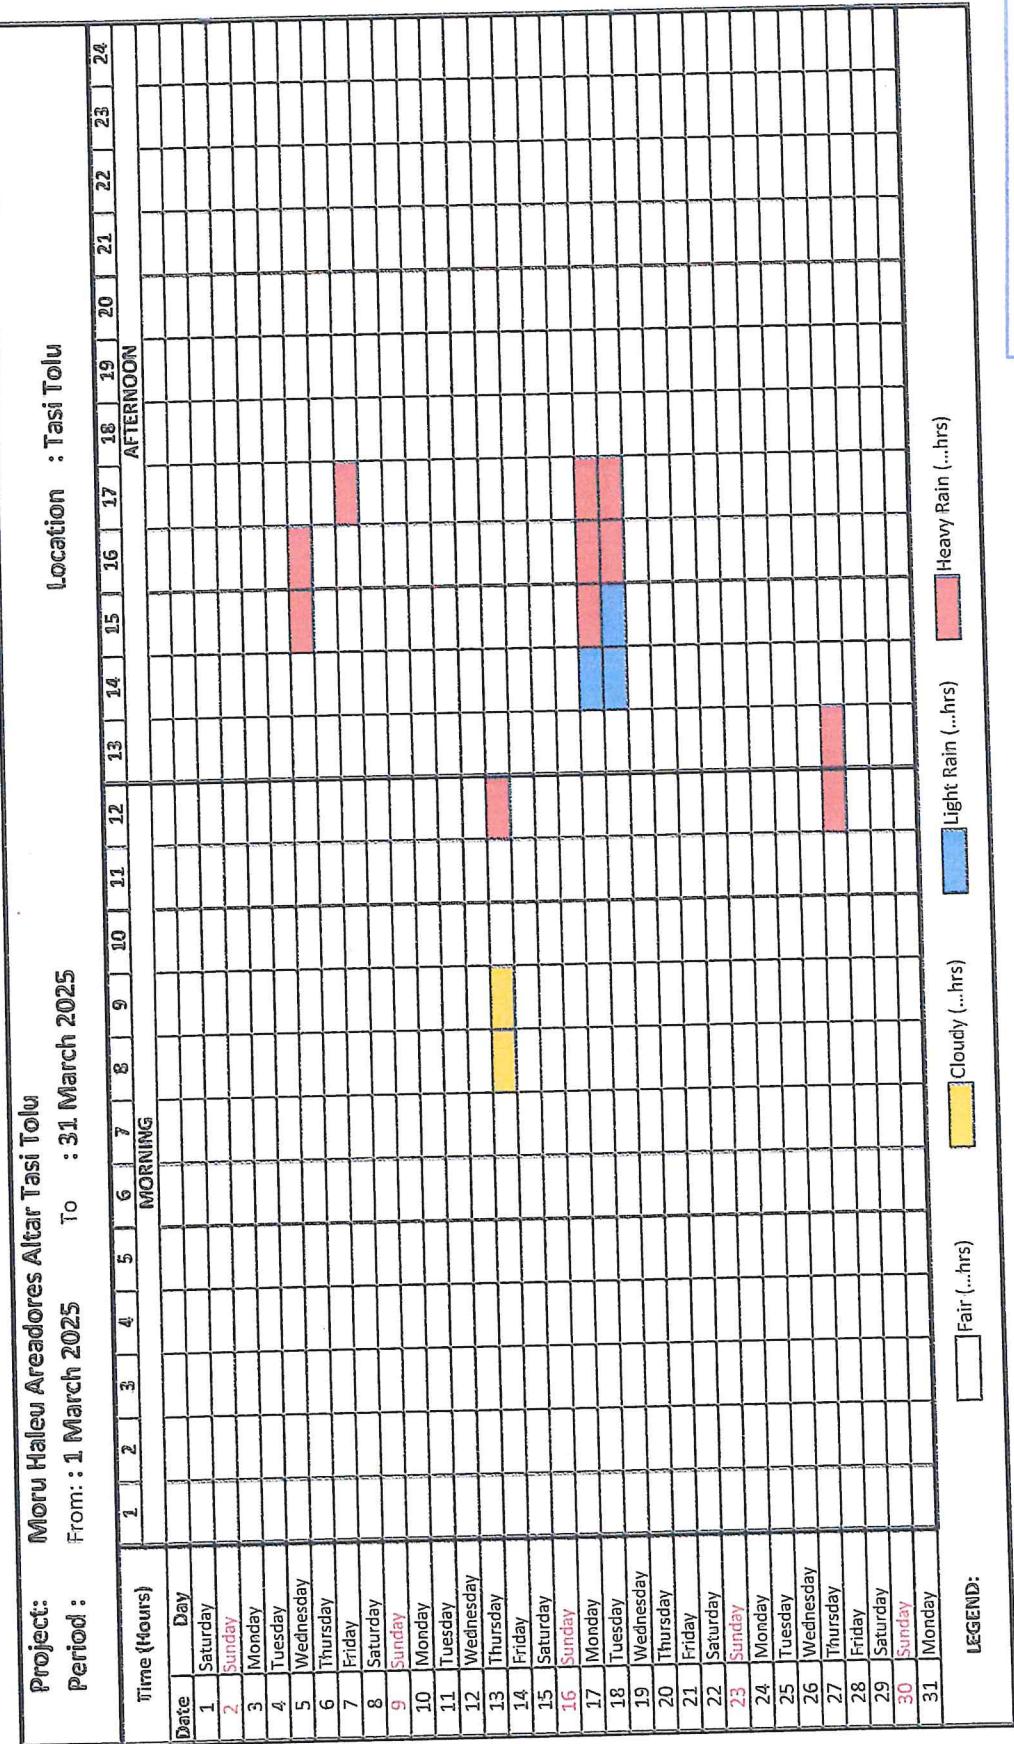
**Robena Engineering Team**  
MOVING FORWARD WITH CONSTRUCTION



**Project:** Moru Haleu Areadores Altar Tasi Tolu

**Period :** From : 1 March 2025 To : 31 March 2025

**Location :** Tasi Tolu



**Robena Engineering Team**

MOVING FORWARD WITH CONSTRUCTION



**Project:** Mori Halehi Areadores Altar Tasi Tolu

From : 1 April 2025 To : 30 April 2025

**Project:** Moru Haleu Areadores Altar Tasi Tolu      **Location :** Tasi Tolu

**Period :** From : 1 April 2025      To : 30 April 2025

Time (Hours)	MORNING					AFTERNOON																	
	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23
Date	Day																						
1	Tuesday																						
2	Wednesday																						
3	Thursday																						
4	Friday																						
5	Saturday																						
6	<i>Sunday</i>																						
7	Monday																						
8	Tuesday																						
9	Wednesday																						
10	Thursday																						
11	Friday																						
12	Saturday																						
13	<i>Sunday</i>																						
14	Monday																						
15	Tuesday																						
16	Wednesday																						
17	Thursday																						
18	Friday																						
19	Saturday																						
20	<i>Sunday</i>																						
21	Monday																						
22	Tuesday																						
23	Wednesday																						
24	Thursday																						
25	Friday																						
26	Saturday																						
27	<i>Sunday</i>																						
28	Monday																						
29	Tuesday																						
30	Wednesday																						

**LEGEND:**

- Fair (...hrs)
- Cloudy (...hrs)
- Light Rain (...hrs)
- Heavy Rain (...hrs)

**LEGEND:**

Fair (...hrs)

Light Rain (...hrs)

THEORY

Robena Engineering Team

MOVING FORWARD WITH CONSTRUCTION
